


Arundel on the Bay



An Exelon Company

November 18, 2013

Bay Ridge – Feeder 8425

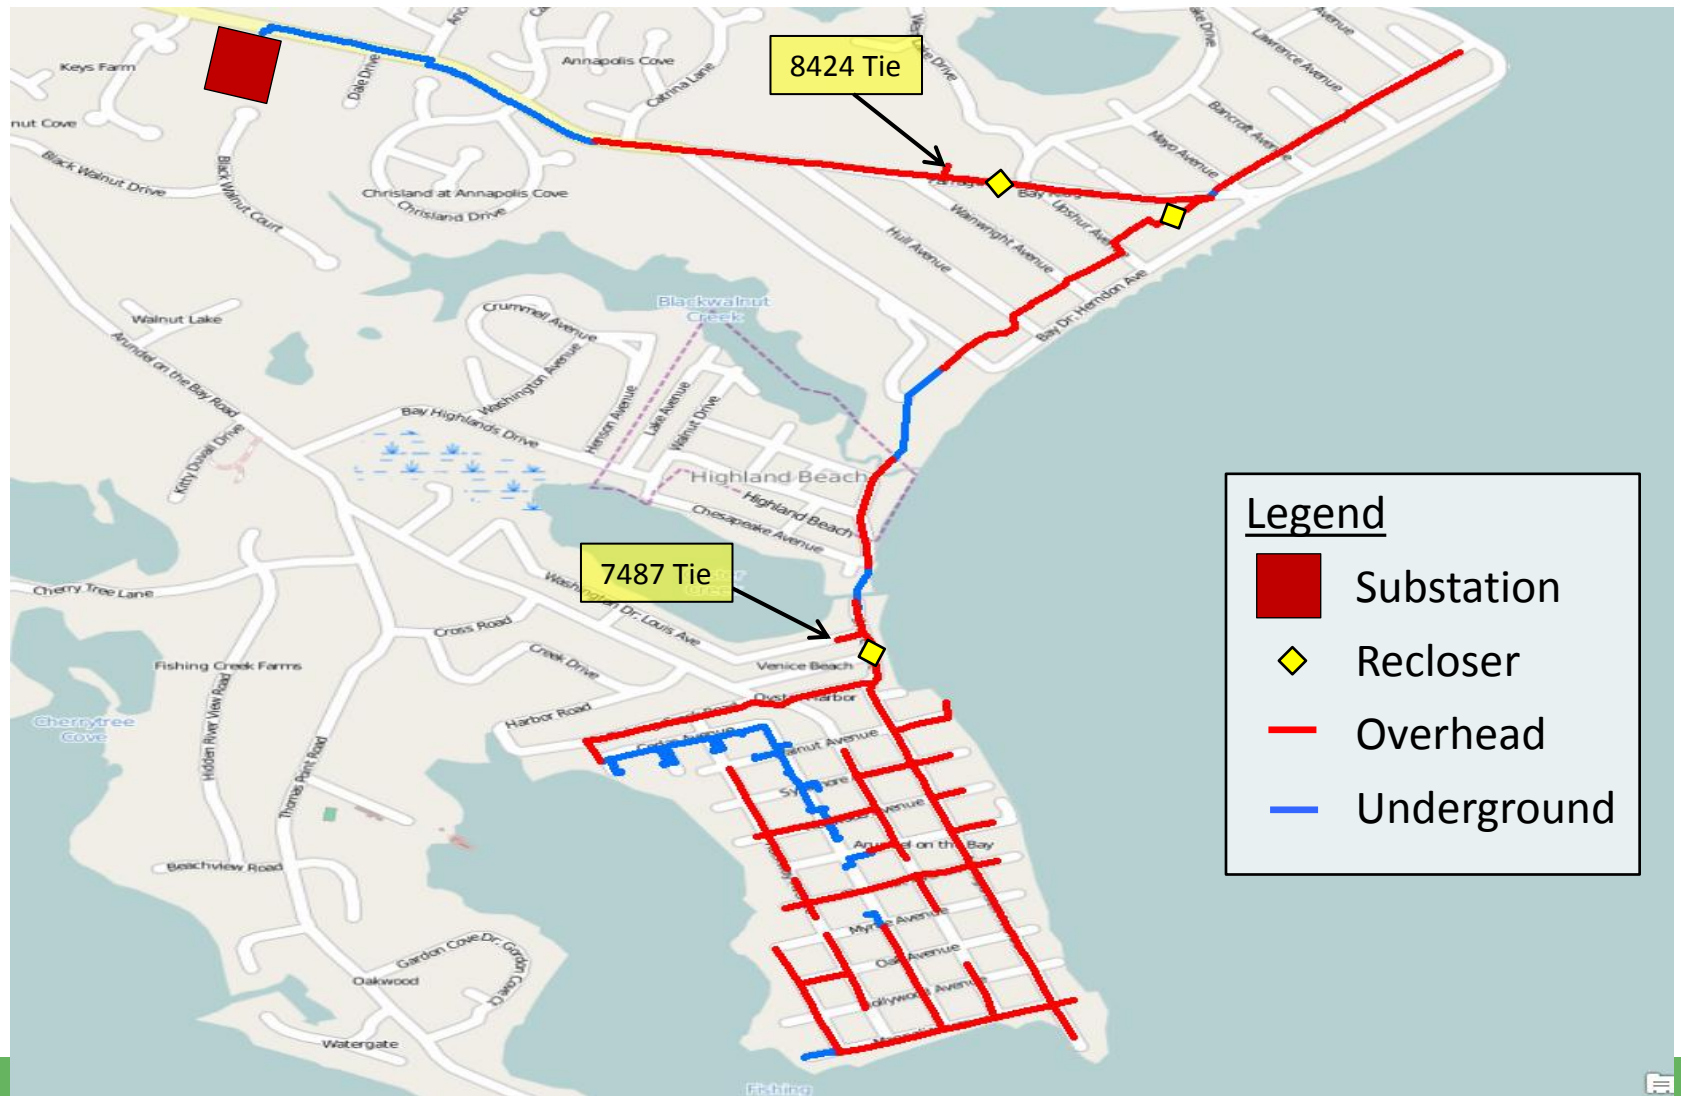

Arundel on the Bay



2013 Performance

2013 Outage History for Arundel on the Bay

-Sustained Outages – 0

-Momentary Outages – 7

<u>Date</u>	<u>Duration</u>
2/9	0 minutes
2/13	0 minutes
5/27	0 minutes
5/29	0 minutes
6/2	0 minutes
8/1	0 minutes
9/12	0 minutes




Reliability Work


- Osprey Pole
 - BGE has been working with President of Bay Ridge Community Center to determine a good location for the New Osprey Nest Pole
 - Though there is a verbal agreement about the location of the new pole, we are still waiting for the customer to complete and return the paperwork that was sent by BGE
 - BGE will continue to reach out to the customer, but if there is a better contact that AOTB officials know of, that would be extremely helpful
- Re-conductor Jobs
 - BGE addressed the two major problematic areas by re-conductoring with new overhead wire in two phases
 - Phase 1 (Complete)
 - New OH wire along Farragut Rd, between Wainwright Ave and Bay Dr.
 - Phase 2 (Complete)
 - New OH wire just off Bay Drive, between Farragut Rd and Herndon Ave
- Installation of New Distribution Automation Equipment
 - Creating a Remote Tie to adjacent feeder
 - This will be complete prior to summer 2014



Re-Conductor – Phase 1

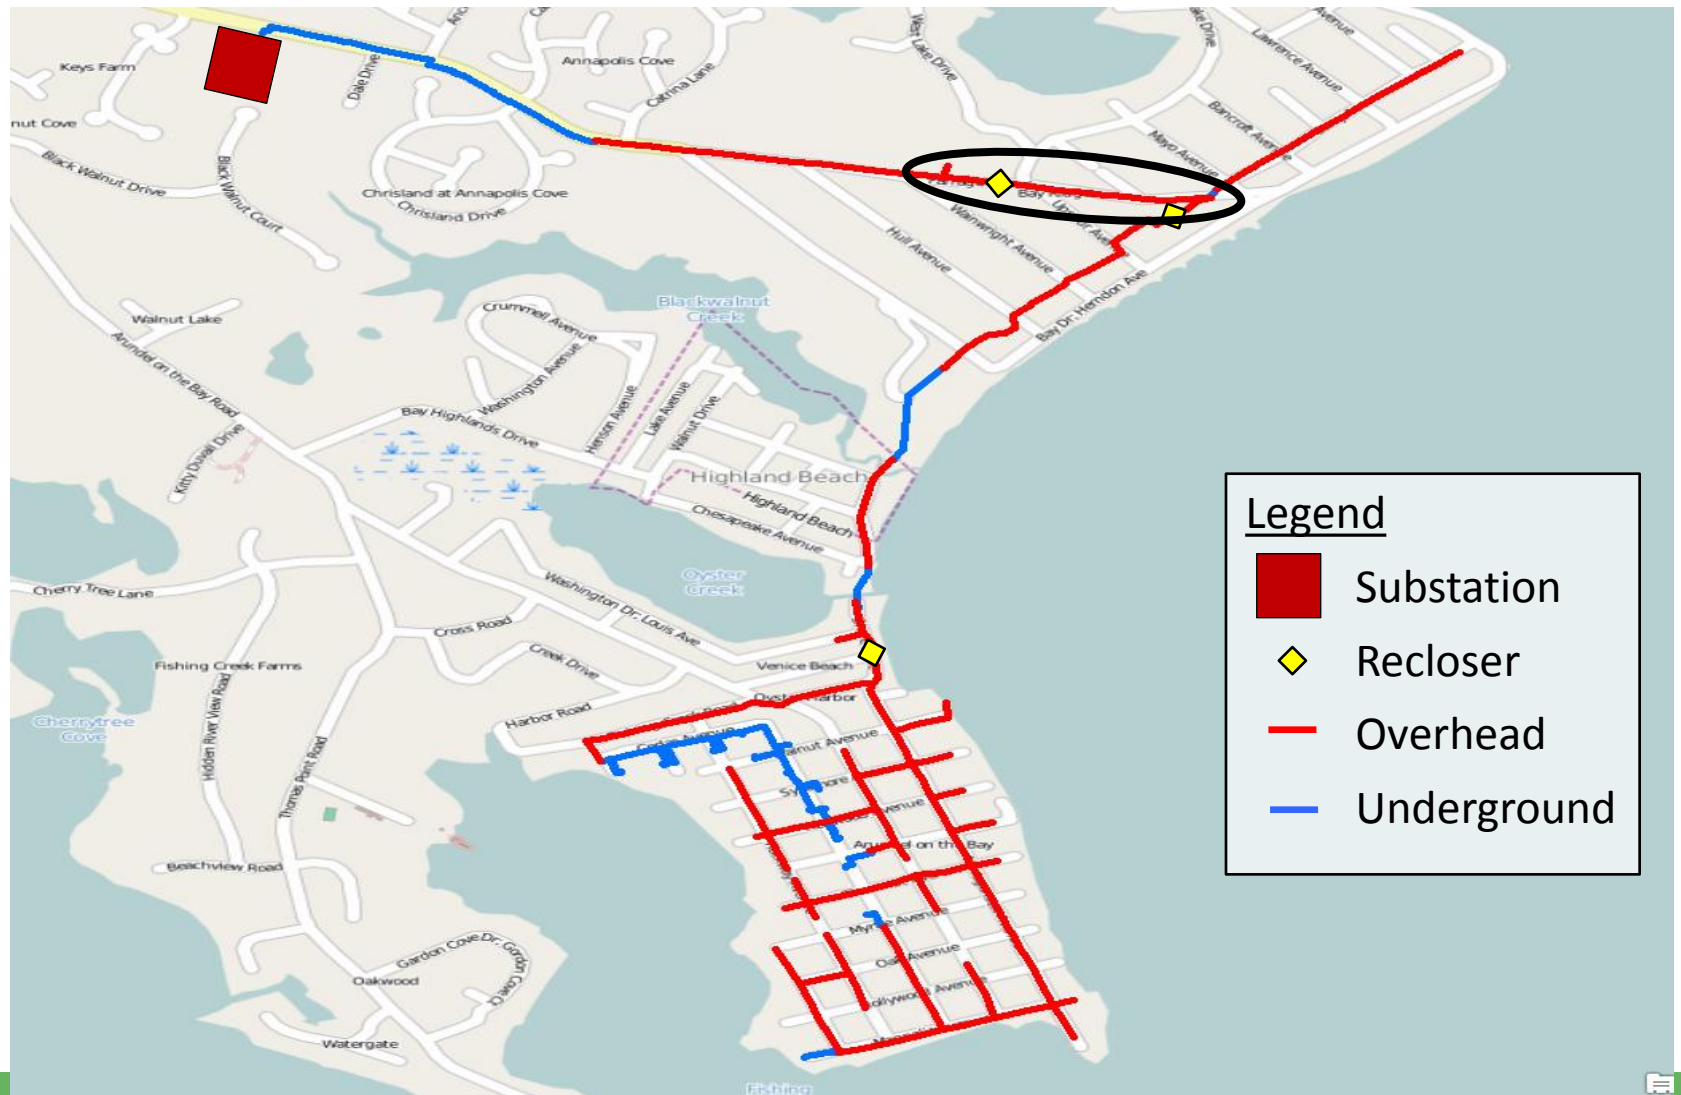

Re-conductor – Phase 2

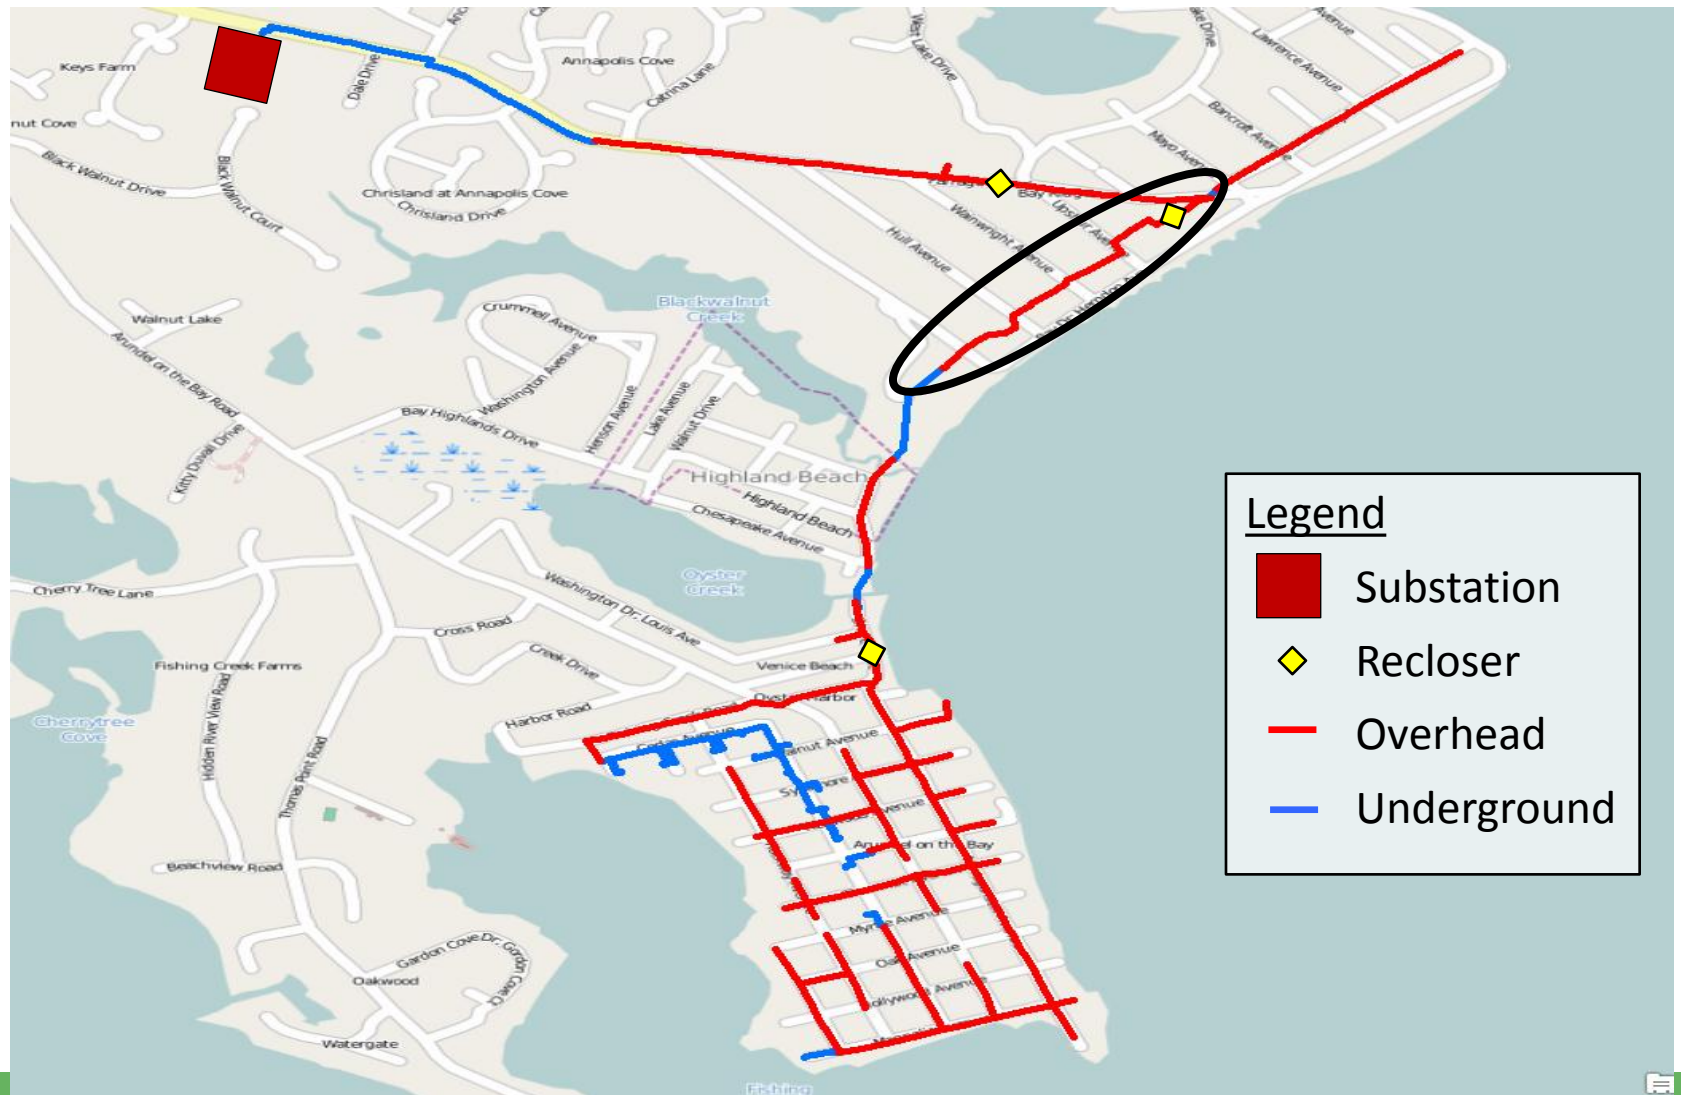

Distribution Automation Install

